

105 Canterbury Ln



Pre-construction Photo

Date Updated:	7/11/2016
Cost Estimate:	\$24,671.06
Est. Project Length:	1 Week
Construction:	Complete
Property Access:	
Utilities:	
Preliminary Eng:	
Right Of Way:	
Construction:	Complete
Contractor:	Brent Scarbrough and Company
Const Start Date:	12/24/2015
Completion Date:	12/31/2015
Problem:	On 12/24/15, approximately 60 homes within the Chanticleer Subdivision were without water and had no access to and from their homes when a 72-inch diameter corrugated metal pipe failed, collapsing the road.
Proposed Solution:	1 - 72-inch RCP pipe with headwall
Percent Complete:	100
Current Status:	Completed
Total Cost:	\$101, 636

Construction Photo



Post Construction Photo

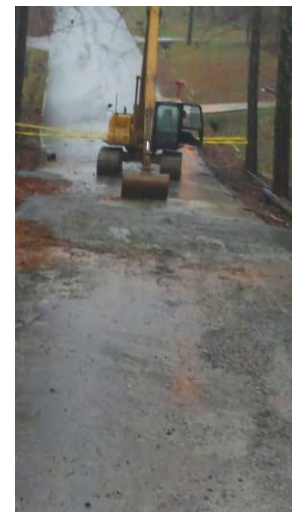




Photo 1: The large collapsed hole in Canterbury Lane was repaired and paved.



Photo 2: Rock was added to the shoulder of the road and around the new pipe and headwall.



Project: 105 Canterbury Lane – 2017 SPLOST

Date: March 2016



Photo 1: Canterbury Lane is being repaired for road reopening.



Photo 2: Photo shows water flowing through the new concrete pipe. Pipe replacement and new headwall installation was successful.



Project: 105 Canterbury Lane – 2017 SPLOST

Date: December 31, 2015



Photo 1: New 72" concrete pipe is being installed. Exposed utility lines are visible in the photo.



Photo 2: New 72" concrete pipe is being installed. Exposed utility lines are visible in the photo.



Project: 105 Canterbury Lane – 2017 SPLOST

Date: December 30, 2015



Photo 1: Site excavation and clean up underway to prepare for new pipe placement.



Photo 2: Site excavation, clean up and water pumping underway to prepare for new pipe placement.



Project: 105 Canterbury Lane – 2017 SPLOST

Date: December 30, 2015



Photo 1: Approximately 60 homes within the Chanticleer Subdivision were without water and had no access to and from their homes when a 72-inch diameter metal pipe failed, collapsing the road.



Photo 2: The metal pipes failed, washed out from under the road, and were found downstream from Canterbury Lane



Project: 105 Canterbury Lane – 2017 SPLOST

Date: December 24, 2015
